

# San Vicente Road Improvement Project

Update #8  
May/June 2015

On September 15, 2014 the County of San Diego Department of Public Works started the San Vicente Road Improvement Project in Ramona. The estimated project completion is Spring 2016.

## Construction Traffic Control Hours (Monday – Friday)

Daytime = 9:00am – 3:00pm

Nighttime = 7:00pm – 5:00am

Please note that we will continue to prioritize Northbound traffic in the morning, and Southbound traffic in the evening. Traffic fines doubled in construction zones.


**No lane closures are allowed on National Oceanic and Atmospheric Administration (NOAA) designated "RED FLAG DAYS"**

## Construction progress in May 2015

- Earthwork cut and fill (including rock breaking)
- Utility joint trench construction from Bunnie King to Chuck Wagon Road
- Continued grading for temporary stage 2 roadway detour traffic shift currently anticipated to be completed by mid-July 2015
- Began installing new 16" waterline between Deviney & Chuck Wagon Road
- Continuing storm drain culvert installations in stage 1 working areas and at driveways
- Signals at Warnock retrofitted with video detection making signal operations more efficient

## Upcoming June 2015 Construction Activity

- Continue cut and fill earthwork operations in stage 1 working areas
- Clearing and Grubbing (between Deviney and Wildcat Canyon)
- Continue grading and construction of transitions for temporary stage 2 roadway detours
- Complete Water main and other utility work in the intersections of Warnock and Wildcat Canyon Road
- Continue utility joint trench construction from Warnock to Deviney
- Continue water line installation from Bunnie King to Chuck Wagon – Vicente Meadows.
- Continue drainage system construction
- Start preparing the road base for phase 1 paving
- Asphalt Paving for stage 2 detour road is tentatively scheduled for the week of June 22
- Proposed 24-hr weekend work anticipated for stage 2 traffic shift (see attached exhibit) 7 pm Friday thru 5 am Monday. June 26-29 between Warnock and Deviney and July 10-13 from Deviney to Wildcat Canyon. Traffic will be open to one directional flow and flagging operations and pilot vehicles will be utilized for the 24-hr weekend work schedule on both proposed weekends.

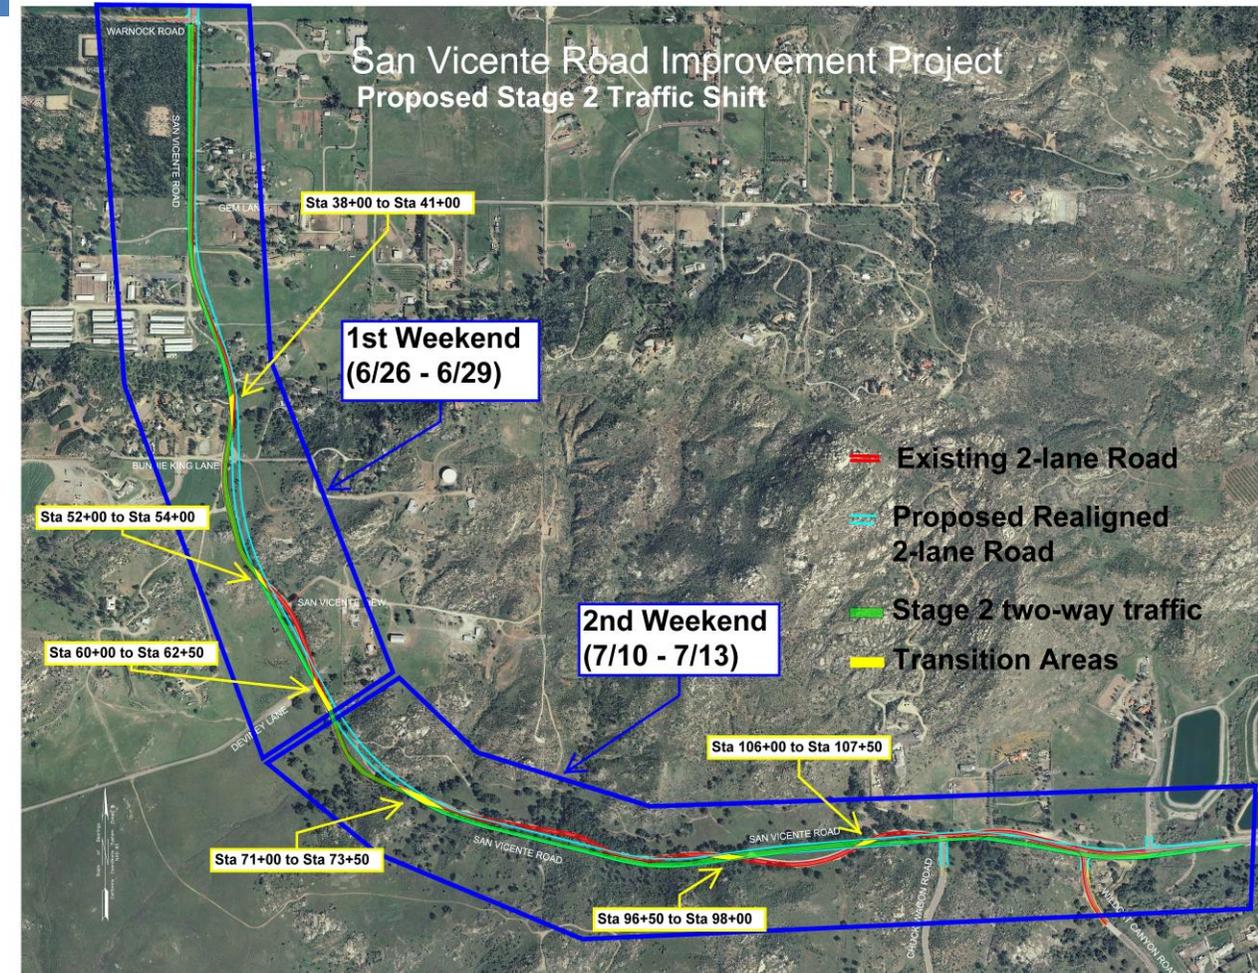

## Construction Warnings and On-going Coordination

- **Please note that an increase in speeding has been observed within the construction limits and traffic fines are doubled in construction zones. For your own safety and the safety of the public and the construction personnel, please use the radar feedback signs and observe the posted 40 MPH construction speed limit.**
- Monthly Emergency Services Meeting was held on Wednesday, June 10, 2015 with County staff, Flatiron Construction, Sheriff, CHP and CalFire to continue coordination for the minimization of traffic delays and planning for stage 2 traffic shift. The next meeting will be on July 8, 2015.
- **\*\*Bicyclists** are encouraged to use an alternative route during construction. Any bicyclists on San Vicente Road during construction are reminded that you are required to share the road with motor vehicles so please use caution.

## Questions?

Call: 1-877-291-6565

Email: SVR@adease.com

